

ISMC221 IS PROJECT MANAGEMENT
Preliminary ExamProject Charter

1

Mark Eric Antonio
Christian Vincent Cabral
Najeeb Hussain
Miguel Toledana
Gian Mori Villanueva

1. Project Title:

- **Galatea: A Virtual Fitting Room Extension**

2. Project Sponsor:

Given the scale and technological requirements of Galatea: A Virtual Fitting Room Extension, hereinafter referred to simply as Galatea, it requires significant financial backing. The following stakeholders are the primary Project Sponsors:

A. Shein

- a. **Role:** Industry Expertise
- b. **Contribution:** Strategic insights about the fashion industry and access to various fashion brands
- c. As one of the world's largest fashion retailers, Shein hopes to tag along with the current wave of advanced technology. The company plans to integrate Galatea into its online shopping platform in hopes for making a revolutionary change in the industry. As such, the company will provide valuable reports and resources as the project progresses.

B. Clarifai

- a. **Role:** Financial sponsor and guidance
- b. **Contribution:** Major funding and consultation for the development phase of Galatea.
- c. Clarifai is an artificial intelligence company that specializes in one of the essential features of Galatea, that being its cutting-edge image processing technology. Taking an interest, the company has decided to provide financial support throughout the execution of the project as well as guidance and workforce for the project's development phase.

3. Project Objectives:

- Project Galatea allows users to find the perfect fit without the need to second guess if what they are buying is their appropriate size by having a virtual fitting room integrated into both mobile and web applications of major fashion businesses like Bench, Penshoppe, and Shein within Q2 of 2024. With this integration, big businesses might want to invest and integrate our project into their mobile/web applications.

4. Project Scope:

- This project's scope includes the mobile and web applications of various fashion businesses like Shein, Bench, and Penshoppe. The team would only be developing a module that would be integrated with the existing application that the business has. The project only limits itself to fashion businesses since they are the one that needs this virtual fitting room.

5. Stakeholders:

Project Galatea is an information technology project that aims to improve the user experience of online clothing stores' websites and/or applications. The Project Stakeholders are listed below:

A. Customers

- the end users of the product. This project is being developed to enhance their experience with regards to virtually shopping for clothes.

B. Sponsors/Executives

- who will mostly benefit from the project. This project will be implemented as an extension to their already existing website and/or application to offer the virtual fitting room feature to their customers. They are also the ones who determine how the project's development will proceed.

C. Employees

a. Managers

- oversees the various development stages of the project. Responsible for keeping track of team members' progress, as well as keeping the sponsors and executives informed about the project's development.

b. Project Team

- responsible for developing and completing the project. Tasked with the whole development of the project, starting from planning until monitoring and maintaining.

c. Marketing Team

- tasked with reaching out to the external customers. The marketing team will be working closely with the project team to spread news of the project to potential customers.

d. Finance Team

- responsible for distributing the funds for the project's development. The finance team shall hold the funding for Project Galatea and will determine which section of the project development will be given priority with regards to monetary assistance.

D. Competitors

- will be affecting how successful the project will be. Upon the implementation of the project, the competitors' response needs to be monitored to determine whether further actions are necessary.

E. Government

- involved due to policies and regulations with regards to customer data. All related policies and regulations must be followed before the implementation of the project to ensure customer data integrity and privacy.

6. Initial Requirements:

Galatea is an IT project that proposes the integration of a clothes-fitting feature into the business's web/mobile application. Similar to the concept of dress-up games, the customers can dress up a customizable virtual mannequin that resembles them and pick different clothing or outfits from the vast array of clothes being offered by the business. Now, to ensure a successful project and flawless execution from start to finish, Galatea requires the following deliverables at its initial stage:

- Initial Prototype / Blueprint - This is an important step to ensure an efficient development stage.

- High-Level Timeline - As the project progresses, there will be instances where a team or individual can finish early or late for a specific milestone/deliverable. Thus, it is crucial to have a timeline that will allow the teams and individuals to control the schedule and make adjustments.
- Budget Approval - The approved budget is required in order to purchase or avail resources that are needed throughout the project timeline.
- Finalized Software Stack - A set of technology/software is required to avoid unwanted delays as the project enters the development stage.

Due to its technicality, the project requires the following:

Front End Development:

- Frameworks and Libraries - Having a set of frameworks and libraries for the development phase will boost the efficiency of the tech team.
- User Interface and User Experience Design

Back End Development:

- Libraries - Libraries pertaining to image processing, machine learning, and artificial intelligence are necessary for the main feature of the software.
- Database - A reliable database is required to handle a wide range of clothing catalogs with minimal issues.
- Third-Party Integrations - Fashion Brands are responsible for the clothing data. Thus, integrations from these brands are required.

Miscellaneous:

- Resources - This includes the budget, services, and amenities for the stakeholders of the project.

Meanwhile, the software itself requires the following essential features:

- AI and Image Processing Capabilities
- Wide Range of Clothing Catalog
- User Profile Management
- Interactive Features

7. Assumptions:

- Regulatory Compliance - all workers in the company will follow instructions and comply with rules and regulations while working on the project
- Full workforce - all job openings will be occupied so that we can work optimally
- All features are preplanned - all features in the application are already stated and in the time table no new features will be added suddenly
- Ahead of the competition - our application will be at the forefront of its class. With

features not found in our camper tires or better in its capabilities

- Main stakeholders support - the main stakeholders are assumed to be supportive in the development of the project and giving the required resources
- Commitment to Project Objectives - all people involved in the project are expected to give their all in developing the project.
- Disaster free - we are assuming no natural disasters will occur during the development of the project ie power outages, typhoons, etc. meaning we can follow the time table without any problems uncontrollable by humans

8. Risks:

- Budget Constraints - given our budget of P7,907,000 which is enough for about 10 months if we ever run into any problems that require budget we would need to reallocate some of the budget cutting our time available to run which is 3 months of the 10 months.
- Technological Constraints - the technology used in the project is fairly new and is still in the early stages of development some features might be outdated while we are working on the project
- Time Constraints - if there are any unforeseen events we will go over the time allocated for the project which is 7 months
- Market competition - more companies are researching ways to include this type of software. There is a large amount of competition.
- Worker level - with our budget we are expected to hire low-mid tier workers which means workers with 5 years of experience or less so that we can keep cost optimal but skills may be lacking in some areas.

9. High-Level Timeline

Timeline Summary

Start Date	End Date	Task
January 4, 2024	January 17, 2024	Project Initiation
January 18, 2024	January 31, 2024	Requirements Gathering
February 1, 2024	February 29, 2024	Design Phase

March 1, 2024	March 28, 2024	Development Phase 1
March 29, 2024	April 25, 2024	Development Phase 2
April 26, 2024	May 23, 2024	Testing Phase
May 24, 2024	June 6, 2024	Implementation
June 7, 2024	June 20, 2024	User Training & Documentation
June 21, 2024	July 4, 2024	Project Closure

Tool Used: *monday.com*

Reference Link for the figures:
<https://gbox119388.monday.com/boards/6659758069/views/144901078>

Galatea Project Timeline [Main Tab...](#) | [Gan...](#) | [Calend...](#) | [Kanb...](#) | [More](#) ▾ | [+](#)

[New project](#) ▾ 🔍 Search 👤 Person ⚙ Filter ▾ ⬆ Sort ⚙ Hide ...

▾ **To-do**

☐	Project		Status ⓘ	Due date ⓘ	Priority	Timeline ⓘ	Dependency ⓘ
☐	▸ Testing Phase 2	⊕	Working on it	🕒 May 23	Critical ⚠	Apr 26 - May 23	Development Phase 2
☐	Implementation	⊕	Not Started	🕒 Jun 6	Critical ⚠	May 24 - Jun 6	Testing Phase
☐	User Training & Docume...	⊕	Not Started	🕒 Jun 20	High	Jun 7 - 20	Implementation
☐	Project Closure	⊕	Not Started	🕒 Jul 4	High	Jun 21 - Jul 4	User Training & Docu...
☐	+ Add project						
				May 23 - Jul 4		Apr 26 - Jul 4	

▾ **Completed**

☐	Project		Status ⓘ	Due date ⓘ	Priority	Timeline ⓘ	Dependency ⓘ
☐	Project Initiation	⊕	Done	🕒 Jan 17	High	! Jan 4 - 17	
☐	▸ Development Phase 2 2	⊕	Done	🕒 Apr 25	Critical ⚠	! Apr 25	Development Phase 1
☐	Design Phase	⊕	Done	🕒 Feb 29	Critical ⚠	! Feb 29	Requirements Gathe...
☐	▸ Development Phase 1 2	⊕	Done	🕒 Mar 28	Critical ⚠	! Mar 28	Design Phase
☐	Requirements Gathering	⊕	Done	🕒 Jan 31	High	! Jan 18 - 31	Project Initiation
☐	+ Add project						
				Jan 17 - Apr 25		Jan 4 - Apr 25	

Figure 1. Project Timeline Main Table

Notes: Timelines with diamond figures indicate milestones.

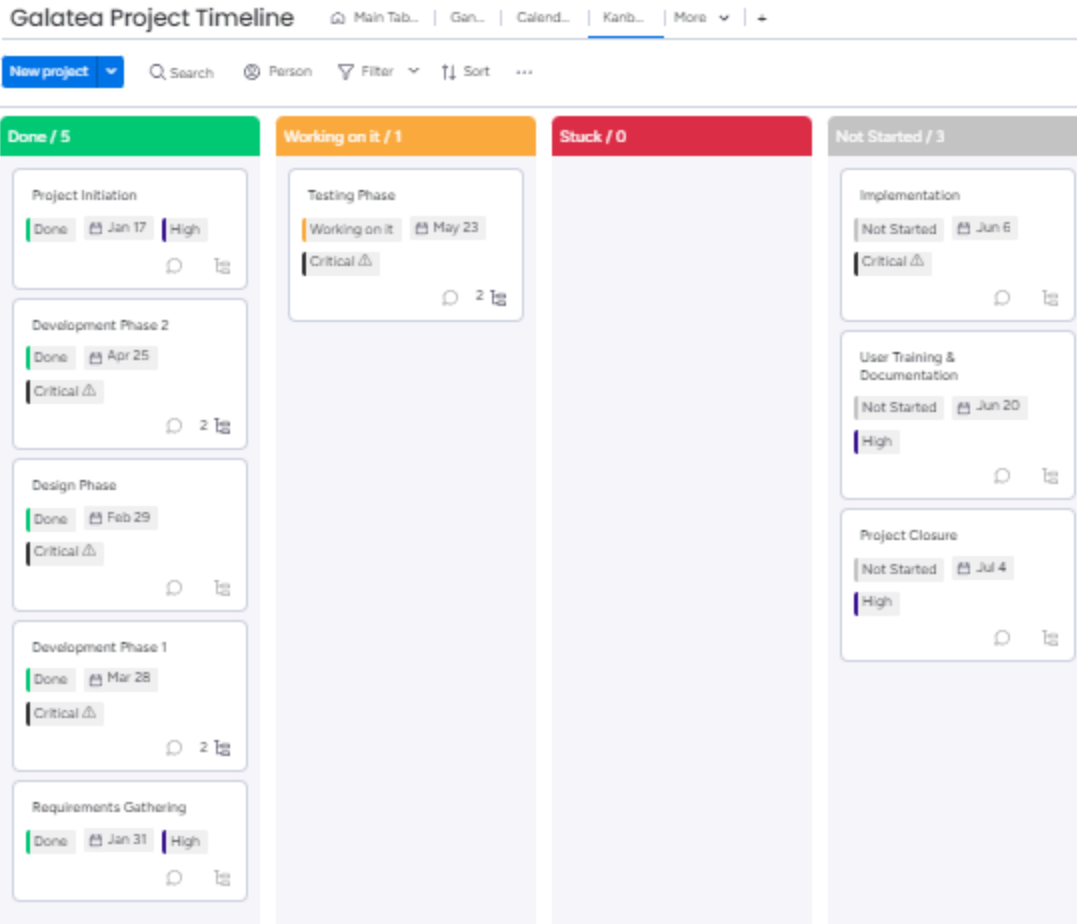


Figure 2. Project Timeline Kanban

10. Budget:

Budget Estimation	
Development Costs	
UI/UX Designer (2 - 4 Job Positions)	P45,000/mo
Developer (8 - 10 Job Positions)	P49,000/mo
Data Scientist (2 - 3 Job Positions)	P50,000/mo
AI Engineer (2 - 3 Job Positions)	P90,000/mo
Services and Infrastructure Costs	

Cloud Services	P110,000/mo
Testing and Quality Assurance Costs	
QA Engineer (2 - 3 Job Positions)	P27,000/mo
Beta Testing Programs	P30,000
Marketing and Promotion	
Advertisements	P50,000
Miscellaneous	
Office Rent and Utilities	P200,000
Hardware/Software Equipment	P100,000

Estimated Cost: ~P7,907,000

This estimated cost is based on the maximum number of job positions for each available job in this Project.

11. Project Approval:

PROJECT NAME	Galatea: A Virtual Fitting Room Extension		
JOB LOCATION	Website/Application Extension		
EST. START DATE	January 4, 2024	EST. FINISH DATE	June 21, 2024
PROJECT LEADER	Gian Mori U. Villanueva	COMPANY	IS Project Management
CONTACT NAME	Gian Villanueva	ADDRESS	Kalye Trese Brgy. Sta. Cruz, Naga City, Camarines Sur
PHONE	09761035179		
EMAIL	gm villanueva@gbox.adnu.edu.ph		

SUMMARY	Creating an extension for clothing store websites and applications that offer the feature of virtually fitting clothes.
DESIRED OUTCOME	An extension file that can be implemented on multiple websites and applications to offer virtual fitting room service.
ACTION TO COMPLETION	Planning, Analysis, Design, Developing, Testing, Implementation, Monitoring and Maintenance
BENEFITS OF PROJECT	Providing users the enhanced experience of being able to try the clothes they plan to buy online. Partnered clothing stores who integrated the project will be able to attract more customers.
PROJECTED SCHEDULE	Project Galatea is projected to be complete within six (6) months, starting from January 2024 until late June 2024.
PROJECTED BUDGET	The projected budget for Galatea is Php 7, 907, 000.00. This budget includes all the necessary expenses, from the development costs until the miscellaneous for maintenance.
PROJECTED TEAM AND RESOURCE REQUIREMENTS	Project Galatea is expected to be developed by a team consisting of 20 to 30 members, all distributed to various tasks responsibly. The projected resource requirements for this project includes hardware and software for development, and service and infrastructure integration.
PROPOSAL MAY BE WITHDRAWN IF NOT ACCEPTED BY DATE OF	
January 31, 2024	

ACCEPTANCE OF PROPOSAL			
AUTHORIZED CLIENT SIGNATURE		DATE OF ACCEPTANCE	January 15, 2024

References(Task E) [lagay ko lang kung need]

Clarifai, The World's AI Company. (n.d.). *Full stack AI developer platform: Production Computer Vision & LLMS*. Clarifai | the World's AI Company. <https://www.clarifai.com/>

For salaries

<https://ph.indeed.com/career/>

<https://www.glassdoor.com/Salaries/>

<https://www.eriei.com/salary/job/artificial-intelligence-engineer/philippines>

Team, W. (n.d.). *Online advertising costs: How much does it cost to advertise online?* WebFX. <https://www.webfx.com/digital-advertising/pricing/how-much-does-it-cost-to-advertise-online/>
